BRUHAT BANGALORE MAHANAGAR PALIKE

Name of Work: Improvements to Someshwara Hill and surrounding areas at Attur Ward No.03 in Yelahanaka Satelite Town Sub Division

Item No	Description of Work	Unit	BOQ Qty (1)	Executed Qty (2)	Dec-21	Jan-22	Feb-22	Mar-22	Apr-22	May-22	Jun-22	Jul-22
1	KSRRB 200-9. Clearing and grubbing road land including uprooting rank vegetation, grass, brush, shrubs, saplings and trees of girth upto 300mm, by manual means, in area of thorney jungle, removal of stumps, disposal of	SQM	5150	2059.67								
2	KSRRB 300-1. Earthwork excavation by manual means for roads, drains & similar works in ordinary soil excavated surface levelled and sides neatly dressed, the disposed earth to be	CUM	1801.04	2144.64								
3	KSRRB M300-19. Removal of unserviceable soil including excavation, loading and disposal but excluding replacement by suitable soil which shall be paid separately as per clause 300.5	Cum	3516.25	2636.67								
5	KSRRB M2100-10. Providing and laying Plain cement concrete of mix 1:3:6 with OPC @ 220kgs, with crushed 40mm and down size graded granite metal coarse aggregates @0.89cum and fine aggregates @ 0.46cum, in	Cum	418.51	67.22								
6	Providing and laying plain/reinforced cement concrete for side drains using M20 nominal mix concrete with OPC at 300 kgs. With 20mm and down size granite metal course aggregates at 0.69 cum and fine aggregates at 0.43 cum	Cum	255.624	77.70								
7	KSRB 4-1.5 : Providing and laying in position plain cement concrete of Mix M20 with OPC @ 300kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and	Cum	59.2272	55.68								
9	KSRB 5-14: Providing and constructing load bearing wall with solid concrete blocks having block density not less than 1800kg/m3 having a minimum average compressive strength of 4.00 N/mm2 confirming to IS 2185 (Part 1):2005 and	Sqm	462.56	289.45								
10	KSRB15-3.8 : Providing 18mm thick cement plaster in single coat with cement mortar 1:4, to brick masonry including rounding off corners, wherever required smooth rendering, Providing and removing scaffolding, including cost of	Sqm	925.12	705.77								
12	Fabricating providing and erecting in position of MS Hot Dip galvanized sq hallow poles of 132 x132 heavy gauge length 3000mm with MS Hot Dip galvanized grill work as per approved design and drawing of chief architect using 12 x75mm	Sqm	816.06	286.65								
13	KSRB 4-6.1 : Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for foundations, footings, bases of columns for mass concrete including cost of all materials, labour complete as per	Sqm	360.4	232.41								
14	KSRRB - M2300-14: Providing TMT steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, palcing in position, lapping and / or welding wherever	Tn	26.99201	6.41								
19	KSRB 5.2-3 : Providing and constructing granite / trap / basalt size stone masonry in foundation with cement mortar 1:6, stone hammerd dressed in courses not less than 20 cms high,	Cum	426.048	102.12								
21	KSRB 4-1.6 ; Providing and laying in position plain cement concrete of Mix 1:2:4 with OPC @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878 cum	Cum	56.267	17.46								
31	KSRRB M300-14. Excavation for roadwork in soil with hydraulic excavator of 0.9 cum bucket capacity including cutting and loading in tippers, trimming bottom and side slopes, in accordance	Cum	480	652.11								

Asst. Executive Engineer
Project Division
Yelahanka Zone

Scanned by TapScanner

IMPROVEMENTS ... GROUNDING AREAS AT ATTUR

Item No	Description of Work	Unit	BOQ Qty (1)	Executed Qty (2)	Dec-21	Jan-22	Feb-22	Mar-22	Apr-22	May-22	Jun-22	Jul-22
59	Earthwork excavation by manual means for foundations, either in pits or trenches 1.5m and above in width, in soil not exceeding 1.5m, in depth including dressing the bottom and sides	Cum	236.444	56.78								
60	KSRB 2.8 : Providing and Filling in foundation with granite / trap broken metal 100mm. and down size, with approved sand including hand packing, ramming, watering, including cost of all	Cum	9.6	3.60								
61	Providing and injecting chemical emulsion for Pre- constructional Anti-Termite Treatment creating continuous chemical barrier under and around the column pits, walls, trenches, basement excavation, top surface of the plinth	Sqm	31.08	7.02								
62	Providing and laying in position plain cement concrete of mix 1:4:8 with OPC @ 180 kgs, with 40mm and down size graded granite metal coarse aggregates @ 0.85 cum and fine aggregates @ 0.57 cum machine mixed,	Cum	12.4725	8.21								
63	KSRB 5.2-3 : Providing and constructing granite / trap / basalt size stone masonry in foundation with cement mortar 1:6, stone hammerd dressed in courses not less than 20 cms high, bond stones at two m. apart in each course	Cum	9.33255	5.49								
64	KSRB 4.1.6 : Providing and laying in position reinforced cement concrete of design mix M15 with OPC cement @ 240kgs, with 20mm and down size graded granite metal coarse aggregates @ 0.878cum and fine aggregates @	Cum	4.1115	0.93								
65	KSRB 4.2.2 : Providing and laying in position reinforced cement concrete of Design Mix M20 with OPC @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregates @ 0.460 cum	Cum	5.976	9.85								
66	KSRB 4.2.8: Providing and laying in position reinforced cement concrete of design Mix M20 with OPC @ 320kgs, with 20mm and down size graded granite metal coarse aggregates @0.69cum and fine aggregates @ 0.46cum,	Cum	9.76625	10.95								
67	KSRB 4-6.1: Providing and removing centering, shuttering, strutting, propping etc., and removal of form work for foundations, footings, bases of columns for mass concrete including cost of all materials, labour complete as per specifications.	Sqm	15.40	55.14								
68	KSRB 4-6.9 :Providing and removing centering, shuttering, strutting, propping etc., for edges of slabs and breaks in floor including cost of all materials, labour complete as per specifications. Specification No. KBS 4.6.2	Sqm	65.37	97.28								
69	KSRB 5-14 : Providing and constructing precast concrete solid blocks with compressive strength not less than 3.5 Newton per sqm with cement	Sqm	114.27	91.14								
70	KSRB 4.9.2 : Providing T.M.T steel reinforcement for R.C.C work including straightening, cutting, bending, hooking, placing in position, lapping and / or welding wherever required, tying with	Tonne	1.622865	1.83								
71	KSRB 2.3 : Filling available excavated earth (excluding rock) in sides of foundations upto plinth in layers not exceeding 20 cms. In depth, compacting each deposited layer by ramming after watering with lead upto 50 m. and lift upto	Cum	199.063	112.65								
72	Providing 18mm thick cement plaster in single coat with cement mortar to brick masonry incluing rounding off corners wherever required smooth rendering, Providing and removing scaffolding, including cost of materials, labour,	Sqm	101.57	239.34								

Asst. Executive Engineer
Project Division
Yelahanka Zone
BBMP, Bangalore - 92

Scanned by TapScanner

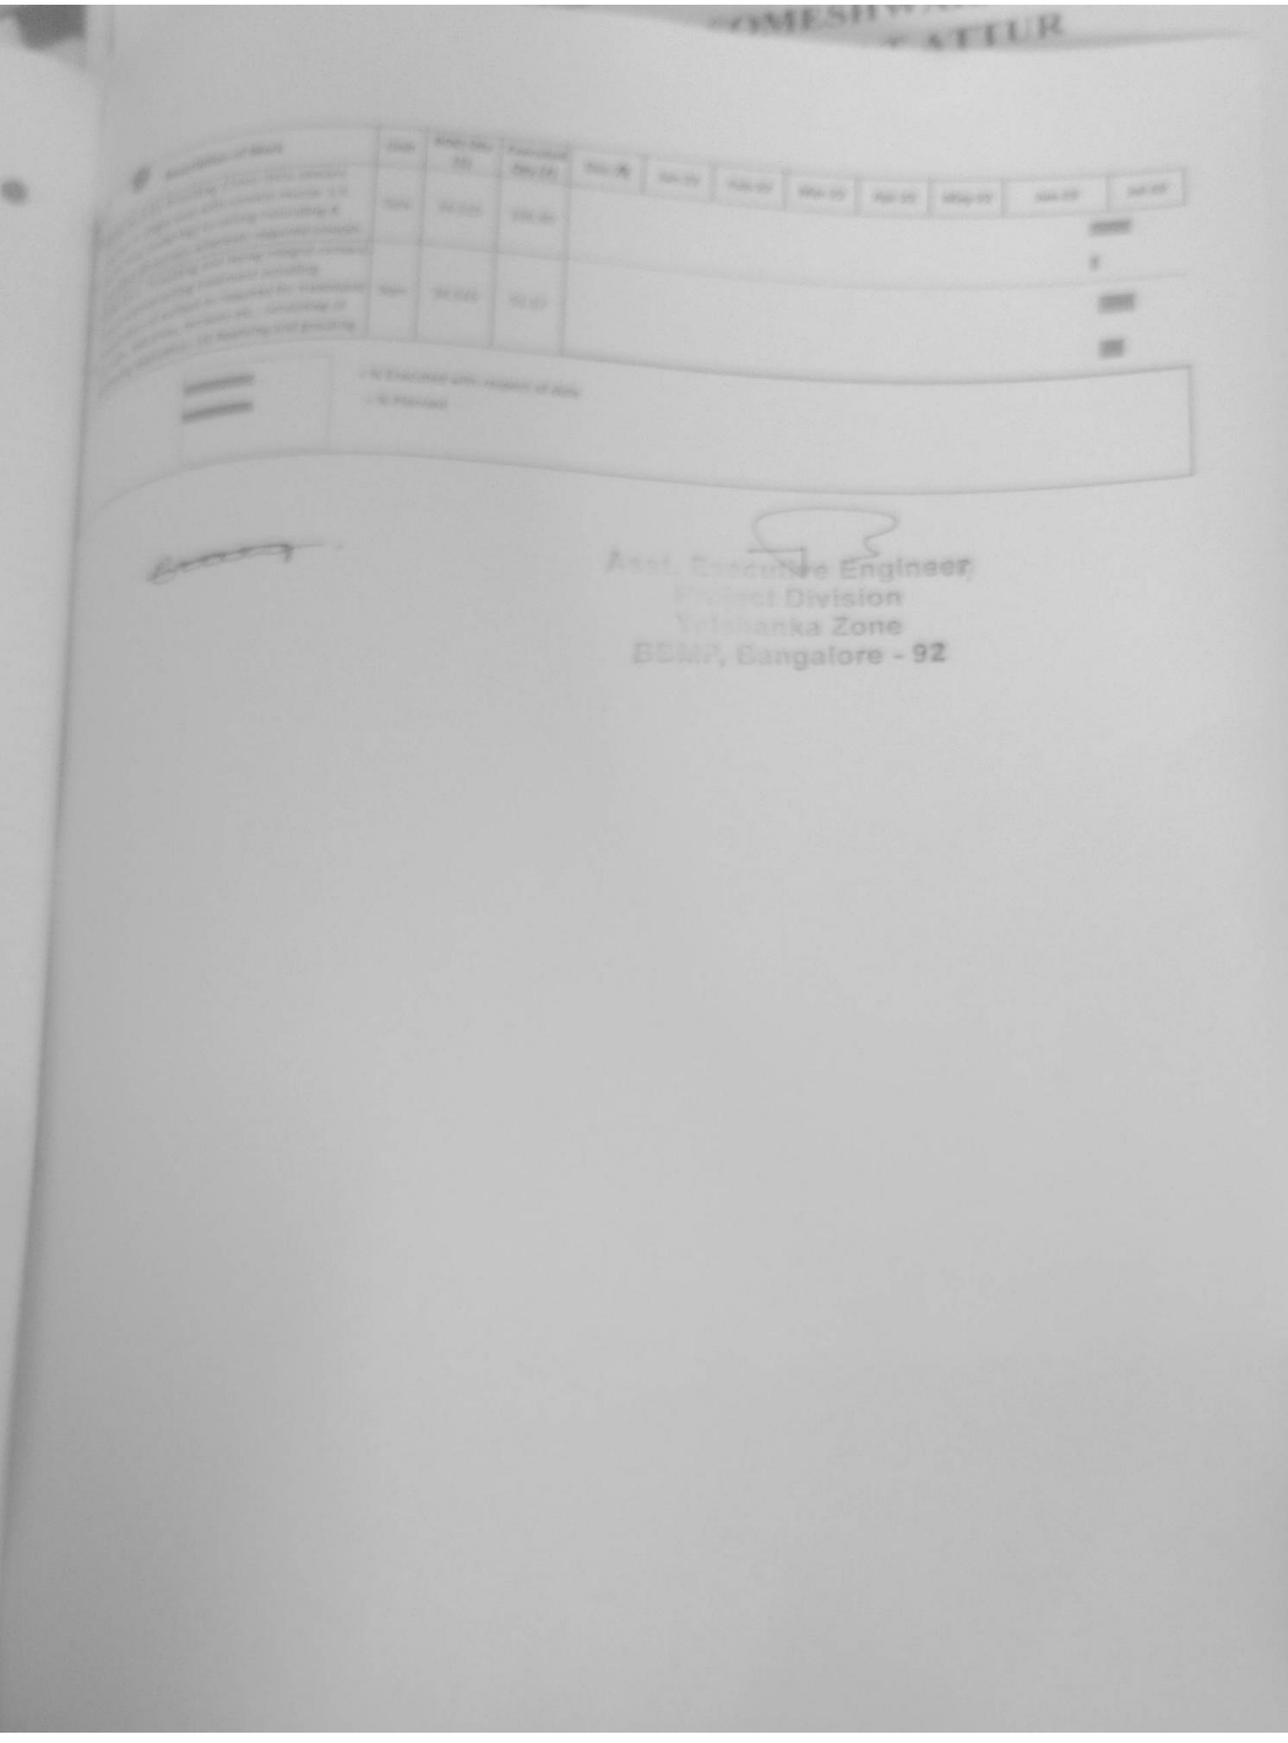

Scanned by TapScanner
